

# OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408  
Auburn, Washington



## JULY 2018 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

**Description:** Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


**Size & Capacity:** 106,000 square feet with 40 classrooms and 800 student capacity.

**Schedule:** Open new and remodeled school August 2019.

**Construction Cost:** \$53,700,000

### CURRENT PROGRESS

Underground storm drainage system.  
Underground water lines.  
Underground electrical and plumbing.  
Utility line connections in adjacent streets.  
Building footings and stem walls.  
Concrete slabs.

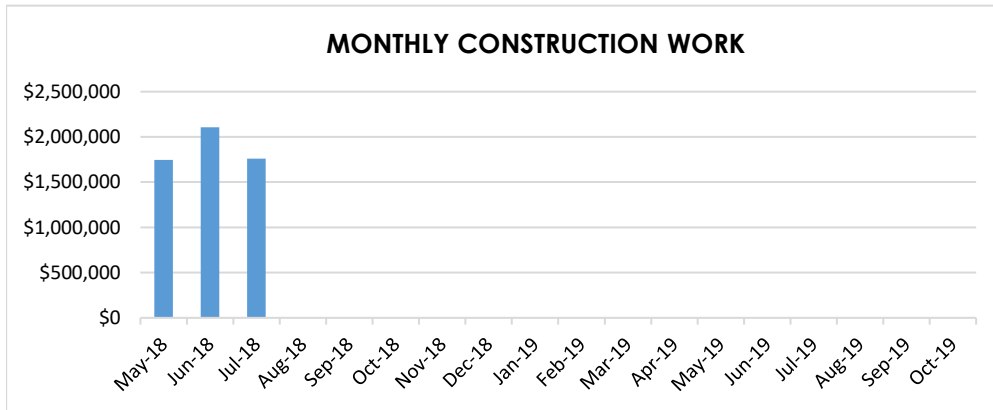

**VALUE OF WORK COMPLETED TO DATE:**  
**\$5,609,376**

**PERCENT OF PROJECT COMPLETE:**  
**10%**

