

# OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408  
Auburn, Washington



## SEPTEMBER 2018 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

**Description:** Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


**Size & Capacity:** 106,000 square feet with 40 classrooms and 800 student capacity.

**Schedule:** Open new and remodeled school August 2019.

**Construction Cost:** \$53,700,000

### CURRENT PROGRESS

- > Underground electrical and plumbing.
- > Concrete slab preparation.
- > Concrete slabs.
- > Gymnasium concrete block masonry.
- > Structural steel erection.
- > East parking lot pavement.
- > H St. underground utilities.

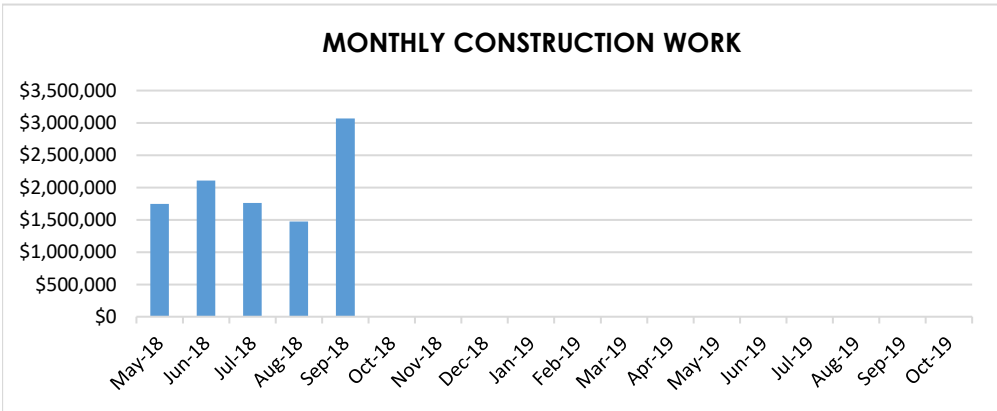

**VALUE OF WORK COMPLETED TO DATE:**  
**\$10,147,807**

**PERCENT OF PROJECT COMPLETE:**  
**19%**

