

OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408
Auburn, Washington



JUNE 2018 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


Size & Capacity: 106,000 square feet with 40 classrooms and 800 student capacity.

Schedule: Open new and remodeled school August 2019.

Construction Cost: \$53,700,000

CURRENT PROGRESS

Site grading, compaction and backfill.
Underground storm drainage structures.
Underground water and sewer lines.
Underground electrical and plumbing.
Utility line connections in adjacent streets.
Building footings.
Elevator shaft foundation.

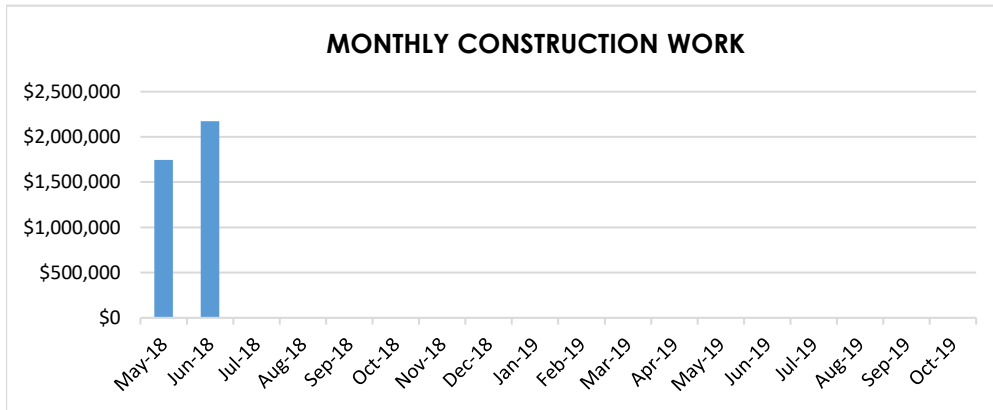

**VALUE OF
WORK
COMPLETED
TO DATE:
\$3,918,703**

**PERCENT
OF
PROJECT
COMPLETE:
7%**

