

OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408
Auburn, Washington



MARCH 2019 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


Size & Capacity: 106,000 square feet with 40 classrooms and 800 student capacity.

Schedule: Open new and remodeled school August 2019.

Construction Cost: \$53,580,000

CURRENT PROGRESS

- > Underground utilities.
- > Exterior waterproofing and brick veneer.
- > Exterior windows.
- > Interior wall framing, wallboard and painting.
- > Mechanical and electrical rough-in.
- > Roofing.

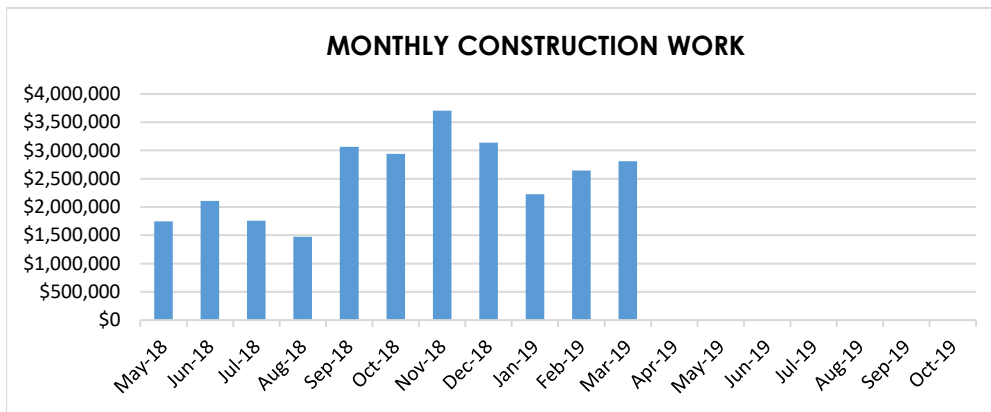

VALUE OF WORK COMPLETED TO DATE:
\$27,616,356

PERCENT OF PROJECT COMPLETE:
52%

