

OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408
Auburn, Washington



APRIL 2019 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


Size & Capacity: 106,000 square feet with 40 classrooms and 800 student capacity.

Schedule: Open new and remodeled school August 2019.

Construction Cost: \$53,580,000

CURRENT PROGRESS

- > Site grading and sidewalks.
- > Exterior waterproofing and brick veneer.
- > Exterior windows.
- > Interior wall framing, wallboard and painting.
- > Interior ceilings and floor tile.
- > Mechanical and electrical rough-in and trim.
- > Roofing.

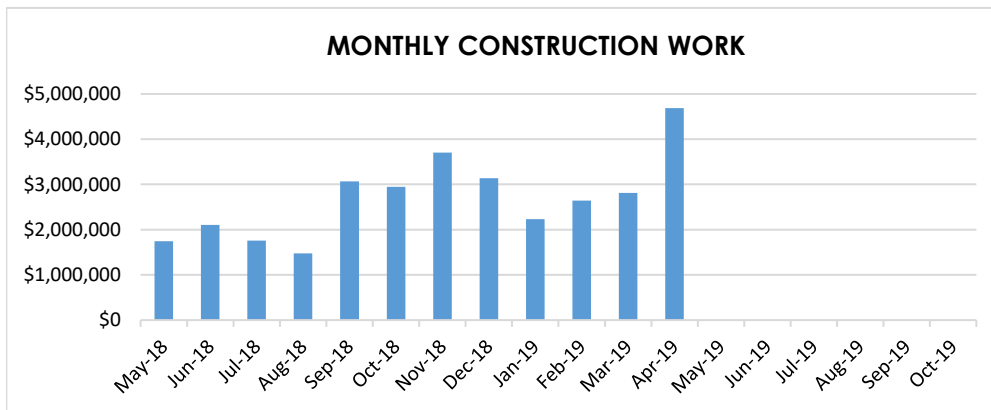

VALUE OF WORK COMPLETED TO DATE:
\$32,305,761

PERCENT OF PROJECT COMPLETE:
60%

