

OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408
Auburn, Washington



MAY 2019 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


Size & Capacity: 106,000 square feet with 40 classrooms and 800 student capacity.

Schedule: Open new and remodeled school August 2019.

Construction Cost: \$53,580,000

CURRENT PROGRESS

- > Sidewalks.
- > Exterior brick veneer and windows.
- > Interior wall framing, wallboard and painting.
- > Interior ceilings, floor tile and cabinets.
- > Mech. and elec. rough-in, trim and fixtures.
- > Equipment start-up.
- > Roofing.

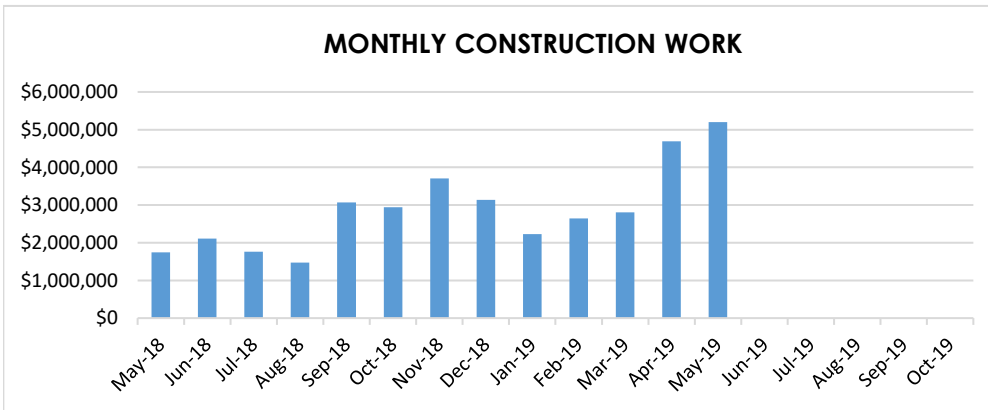

VALUE OF WORK COMPLETED TO DATE:
\$37,506,846

PERCENT OF PROJECT COMPLETE:
70%

