

OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408
Auburn, Washington



NOVEMBER 2018 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


Size & Capacity: 106,000 square feet with 40 classrooms and 800 student capacity.

Schedule: Open new and remodeled school August 2019.

Construction Cost: \$53,580,000

CURRENT PROGRESS

- > East wing concrete block masonry.
- > Structural steel erection.
- > Interior and exterior wall framing.
- > Exterior wall insulation.
- > Mechanical and electrical rough-in.
- > Concrete slabs on metal decks.
- > Mechanical equipment placement.

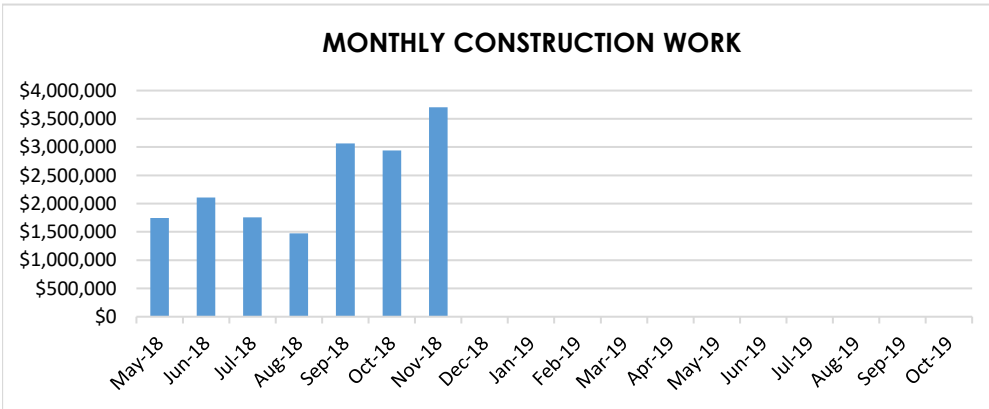

VALUE OF WORK COMPLETED TO DATE:
\$16,796,500

PERCENT OF PROJECT COMPLETE:
31%

