

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




June 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Construction fencing and surveying.
- > Demolition of church and houses.
- > South parking lot storm drainage and sidewalks.
- > Main building abatement and demolition.
- > Site grading and excavation.

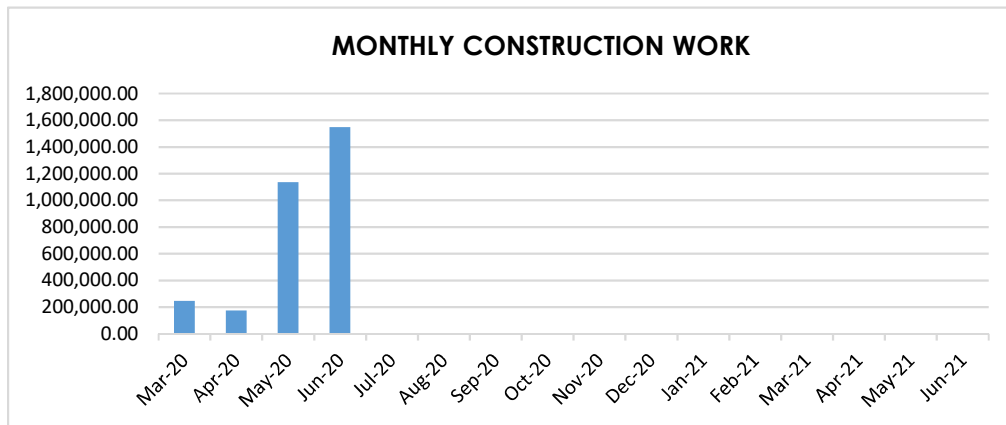

VALUE OF WORK COMPLETED TO DATE:
\$3,101,480

PERCENT OF PROJECT COMPLETE:
7%

