

# BOWMAN CREEK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington




## MAY 2020 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on property located at 5701 Kersey Way SE, Auburn.  
Capacity: 38 classrooms and 650 student capacity.  
Size: 74,413 square feet.  
Schedule: Open new school September 2020.  
Construction Cost: \$46,707,697

### CURRENT PROGRESS

- > Landscaping, irrigation and playfield prep.
- > Sidewalks and asphalt paving.
- > Kersey Way road and wall work.
- > Metal siding, roofing and skylights.
- > Sheetrock, interior finish work and cabinets.
- > Mech. and elec. rough-in and finish work.

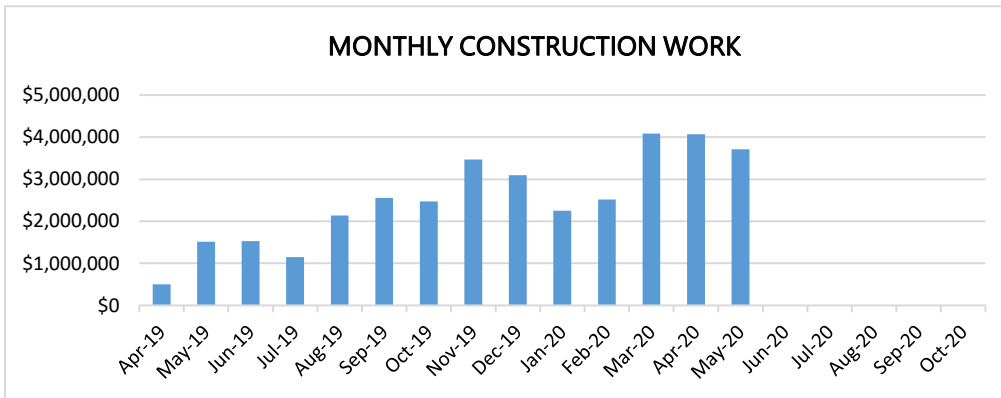

VALUE OF  
WORK  
COMPLETED  
TO DATE:  
**\$35,054,850**

PERCENT  
OF  
PROJECT  
COMPLETE:  
**75%**

