

DICK SCOBEE ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




May 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 1041 14th St. NE, Auburn.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 74,961 square feet.
Schedule: Open new school September 2020.
Construction Cost: \$39,143,452

CURRENT PROGRESS

- > Irrigation, sidewalks and asphalt paving.
- > Readerboard and 14th St. NE road work.
- > Interior finish work, cabinets and carpet.
- > Mech. and elec. rough-in and finish work.
- > Acoustical tile ceilings and exterior doors.
- > Roof flashing and trim.

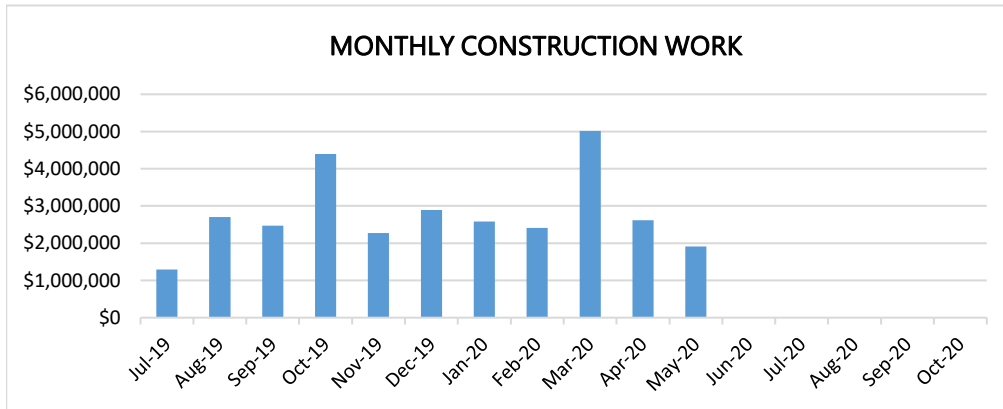

VALUE OF WORK COMPLETED TO DATE:
\$30,565,482

PERCENT OF PROJECT COMPLETE:
78%

