

# BOWMAN CREEK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington




## SEPTEMBER 2020 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on property located at 5701 Kersey Way SE, Auburn.  
Capacity: 38 classrooms and 650 student capacity.  
Size: 74,413 square feet.  
Schedule: Open new school September 2020.  
Construction Cost: \$46,707,697

### CURRENT PROGRESS

- > Punchlist work.
- > Landscaping.
- > Play equipment installation.
- > Mechanical & electrical systems adjustments.
- > Project close out.

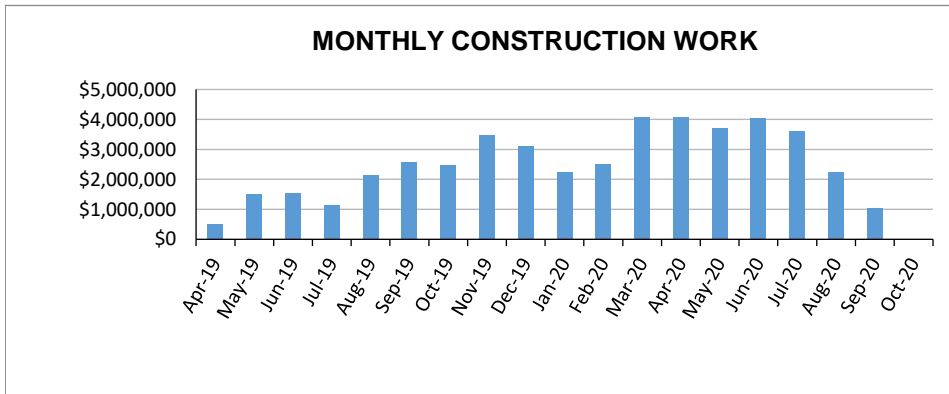

**VALUE OF  
WORK  
COMPLETED  
TO DATE:  
\$42,705,106**

**PERCENT  
OF  
PROJECT  
COMPLETE:  
91%**

