

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



AUGUST 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,075,783

CURRENT PROGRESS

- > Roadway paving, striping and sidewalks.
- > Landscaping.
- > Playground equipment.
- > Door hardware and room signs.
- > Large format displays in classrooms.
- > Owner training and commissioning.

MONTHLY CONSTRUCTION WORK

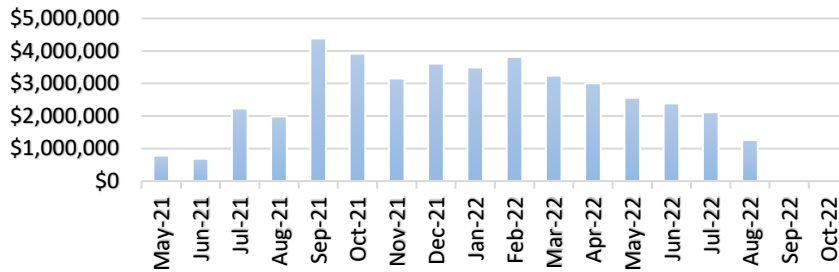

VALUE OF WORK COMPLETED TO DATE:
\$42,653,048

PERCENT OF PROJECT COMPLETE:
93%

