

# CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington



## MARCH 2022 CONSTRUCTION PROGRESS REPORT


### PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA  
Capacity: 38 classrooms and 650 student capacity.  
Size: 73,096 square feet.  
Schedule: Open new school September 2022.  
Construction Cost: \$46,201,746

### CURRENT PROGRESS

- > Landscaping and fencing.
- > Metal roofing.
- > Painting, wallcovering, and wall panels.
- > Walk-in cooler and freezer, and elevator.
- > Ceiling grid and acoustical ceiling panels.
- > HVAC, plumbing, and electrical finishes.

### MONTHLY CONSTRUCTION WORK

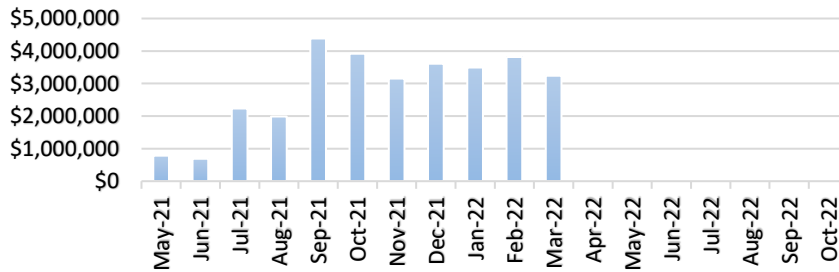

VALUE OF  
WORK  
COMPLETED  
TO DATE:  
**\$31,315,870**

PERCENT  
OF  
PROJECT  
COMPLETE:  
**68%**

