

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



SEPTEMBER 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,112,457

CURRENT PROGRESS

- > Auburn Way South roundabout.
- > Mech. system balancing & commissioning.
- > Punch list work.

MONTHLY CONSTRUCTION WORK

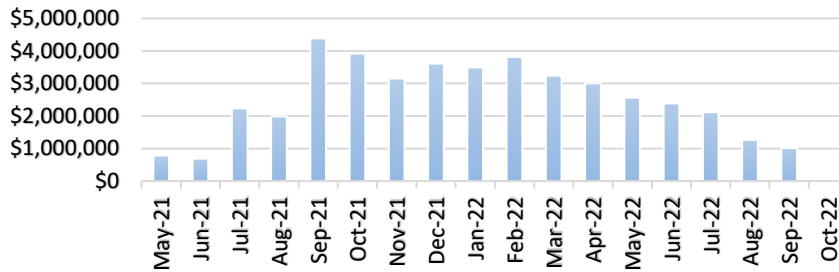

VALUE OF
WORK
COMPLETED
TO DATE:
\$43,666,430

PERCENT
OF
PROJECT
COMPLETE:
95%

