

# CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington



## DECEMBER 2021 CONSTRUCTION PROGRESS REPORT


### PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA  
Capacity: 38 classrooms and 650 student capacity.  
Size: 73,096 square feet.  
Schedule: Open new school September 2022.  
Construction Cost: \$42,999,117

### CURRENT PROGRESS

- > Irrigation and landscaping.
- > Metal floor and roof decking.
- > Exterior siding and masonry.
- > Mechanical, plumbing and electrical rough-in.
- > Interior wall framing and sheet rock.

MONTHLY CONSTRUCTION WORK

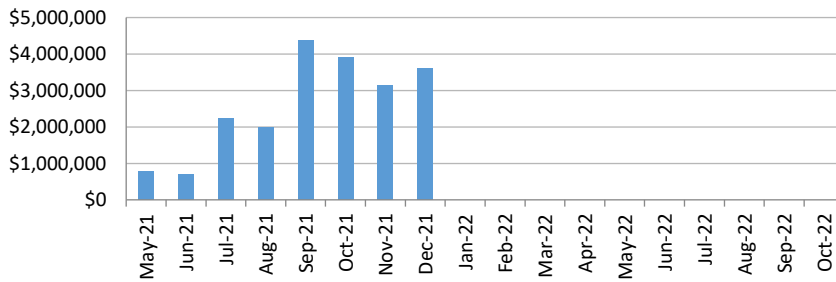

VALUE OF  
WORK  
COMPLETED  
TO DATE:

**\$20,763,687**

PERCENT  
OF  
PROJECT  
COMPLETE:

**48%**

