

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



JUNE 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,242,704

CURRENT PROGRESS

- > Asphalt paving, sidewalks and landscaping.
- > Auburn Way South roundabout.
- > Synthetic turf field surfacing.
- > Floor tile and carpeting.
- > Interior trim and finish work.
- > Mech. and electrical trim and commissioning.

MONTHLY CONSTRUCTION WORK

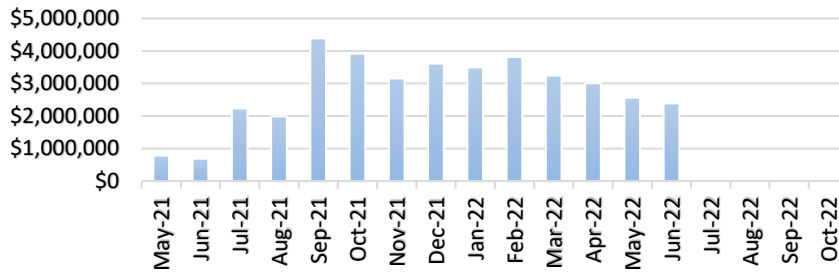

VALUE OF
WORK
COMPLETED
TO DATE:

\$39,270,623

PERCENT
OF
PROJECT
COMPLETE:

85%

