

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




JULY 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$42,537,142

CURRENT PROGRESS

- > Portable classroom removal.
- > Site clearing and excavation.
- > Hazardous materials abatement.
- > Building demolition.
- > Building footings and foundations.
- > Parking lot grading and curbs.

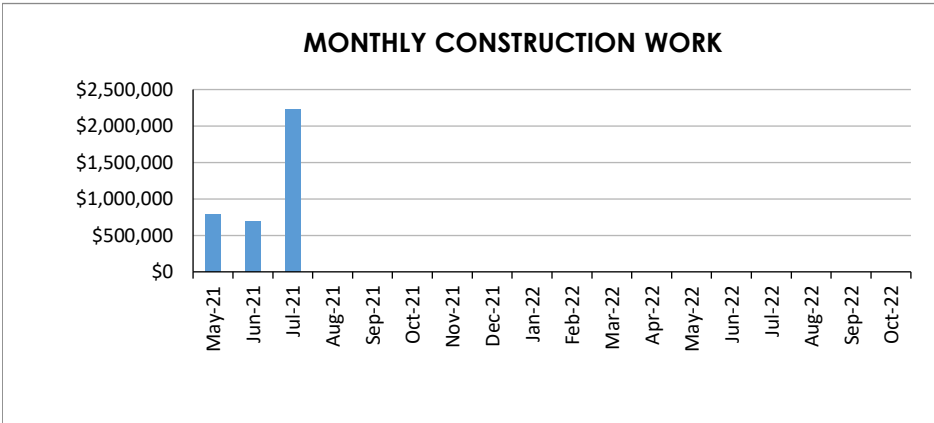

VALUE OF
WORK
COMPLETED
TO DATE:
\$3,708,281

PERCENT
OF
PROJECT
COMPLETE:
9%

