

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



NOVEMBER 2021 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$42,999,117

CURRENT PROGRESS

- > Irrigation system.
- > Metal floor and roof decking.
- > Concrete topping slabs.
- > Interior and exterior wall framing.
- > Exterior wall sheathing.
- > Mechanical and electrical rough-in.

MONTHLY CONSTRUCTION WORK

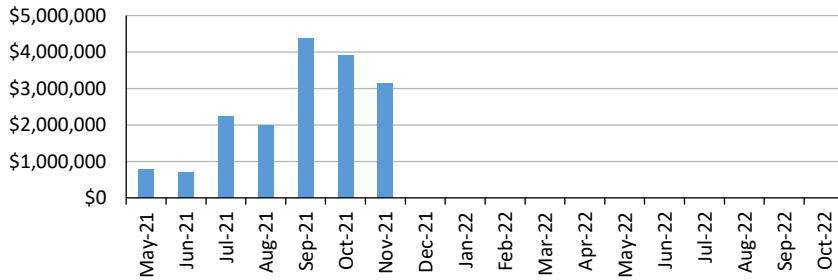

VALUE OF
WORK
COMPLETED
TO DATE:

\$17,153,020

PERCENT
OF
PROJECT
COMPLETE:

40%

