

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




OCTOBER 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$42,846,098

CURRENT PROGRESS

- > Excavation and grading.
- > Curbs, sidewalks and asphalt paving.
- > Concrete floor slab.
- > Structural steel erection.
- > Metal floor and roof decking.
- > Under-slab plumbing and electrical.

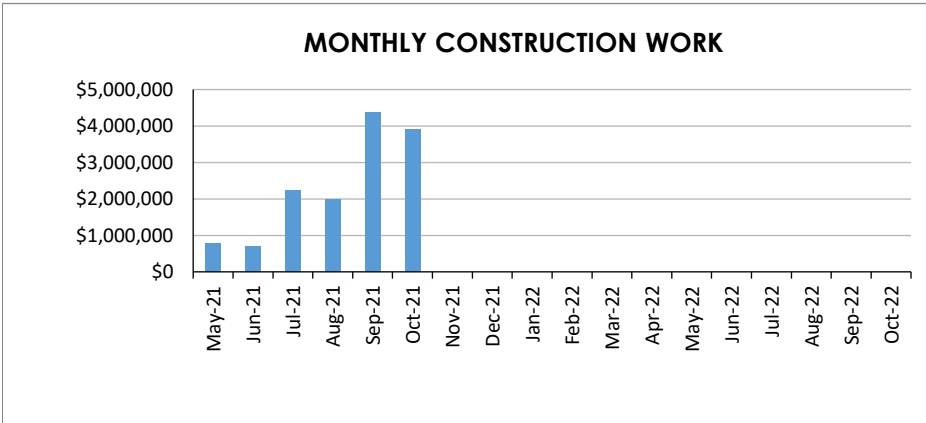

VALUE OF
WORK
COMPLETED
TO DATE:
\$13,998,935

PERCENT
OF
PROJECT
COMPLETE:
33%

