

# CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington




## JANUARY 2022 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA  
Capacity: 38 classrooms and 650 student capacity.  
Size: 73,096 square feet.  
Schedule: Open new school September 2022.  
Construction Cost: \$42,999,117

### CURRENT PROGRESS

- > Roadway and landscaping work.
- > Roof insulation and metal roofing.
- > Exterior siding and masonry.
- > Exterior doors and window frames.
- > Mechanical, plumbing the electrical rough-in.
- > Interior framing, sheet rock and painting.

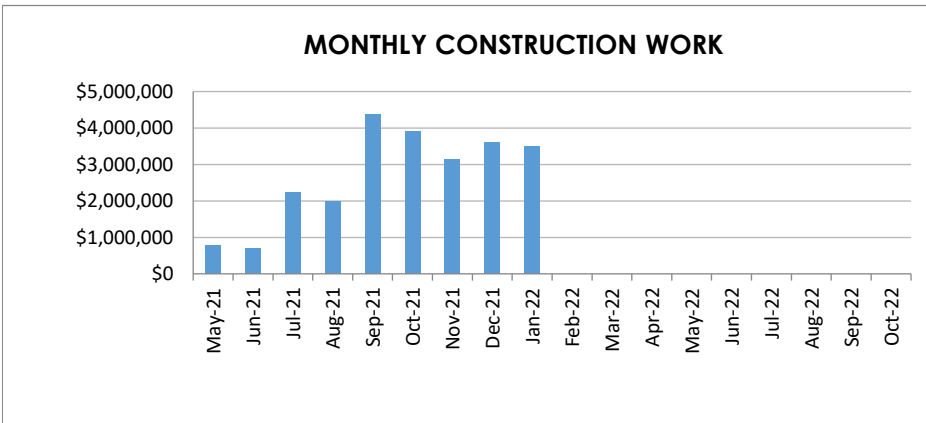

VALUE OF  
WORK  
COMPLETED  
TO DATE:  
**\$24,257,160**

PERCENT  
OF  
PROJECT  
COMPLETE:  
**56%**

