

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



FEBRUARY 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,171,938

CURRENT PROGRESS

- > Masonry, exterior siding and roofing.
- > Window frames and glazing.
- > Cabinets and ceiling grid.
- > Sheetrock and interior painting.
- > HVAC rough-in.
- > Plumbing and electrical finish work.

MONTHLY CONSTRUCTION WORK

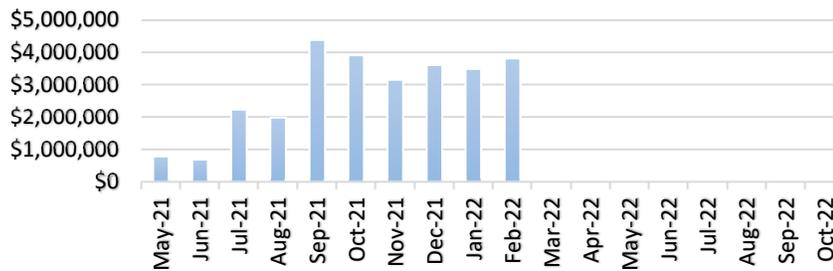

VALUE OF
WORK
COMPLETED
TO DATE:

\$28,074,442

PERCENT
OF
PROJECT
COMPLETE:

61%

