

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



JULY 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,242,704

CURRENT PROGRESS

- > Utilities, paving, and sidewalks at roadway.
- > Sod and shrubs.
- > Carpet and vinyl flooring.
- > Kitchen equipment.
- > Telecommunication systems start-up.
- > Mech. & elec. system commissioning.

MONTHLY CONSTRUCTION WORK

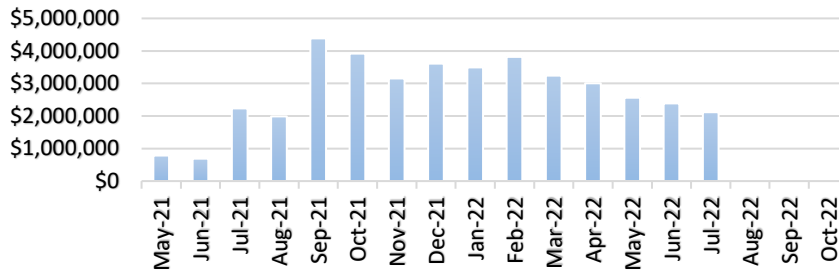

VALUE OF
WORK
COMPLETED
TO DATE:
\$41,387,083

PERCENT
OF
PROJECT
COMPLETE:
89%

