

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



APRIL 2022 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$46,242,704

CURRENT PROGRESS

- > Concrete curbs and sidewalks.
- > Site grading at synthetic turf area.
- > Metal roofing.
- > Painting and wallcoverings.
- > Cabinets, lockers and ceiling grid.
- > Mechanical and electrical equipment and trim.

MONTHLY CONSTRUCTION WORK

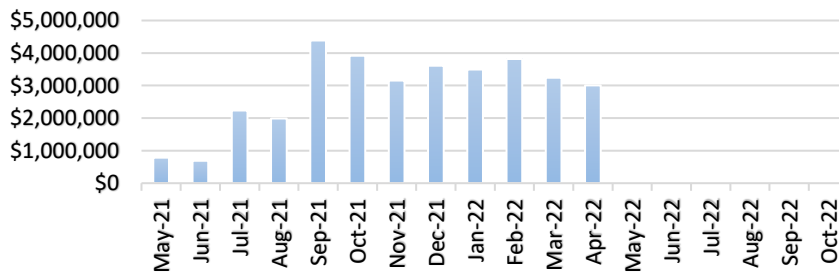

VALUE OF
WORK
COMPLETED
TO DATE:
\$34,321,102

PERCENT
OF
PROJECT
COMPLETE:
74%

