

# CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington



## MAY 2022 CONSTRUCTION PROGRESS REPORT


### PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA  
Capacity: 38 classrooms and 650 student capacity.  
Size: 73,096 square feet.  
Schedule: Open new school September 2022.  
Construction Cost: \$46,242,704

### CURRENT PROGRESS

- > Roadway utilities, grading and curbs.
- > Sidewalks, topsoil, and fences in courtyard.
- > North pathway and playfield drainage system.
- > Carpet, tile and wood gym floor.
- > Kitchen equipment.
- > Mechanical and electrical equipment and trim.

### MONTHLY CONSTRUCTION WORK

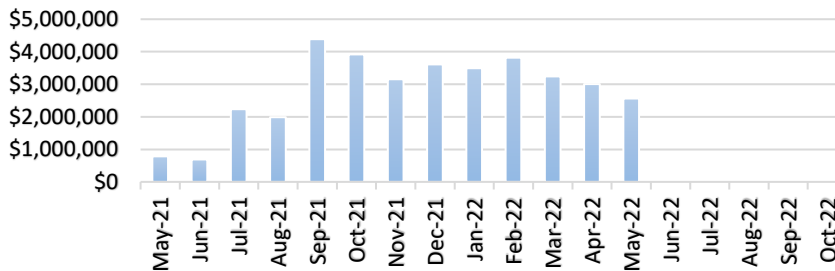

**VALUE OF  
WORK  
COMPLETED  
TO DATE:  
\$36,883,255**

**PERCENT  
OF  
PROJECT  
COMPLETE:  
80%**

