

CHINOOK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




SEPTEMBER 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: New elementary school on existing school property at 3502 Auburn Way S. Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 73,096 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$42,854,075

CURRENT PROGRESS

- > Surplus soil and debris removal.
- > Asphalt paving at parking lots and playground.
- > Concrete curbs and sidewalks.
- > Underground mechanical and electrical.
- > Footings, foundation walls and floor slabs.
- > Steel erection.

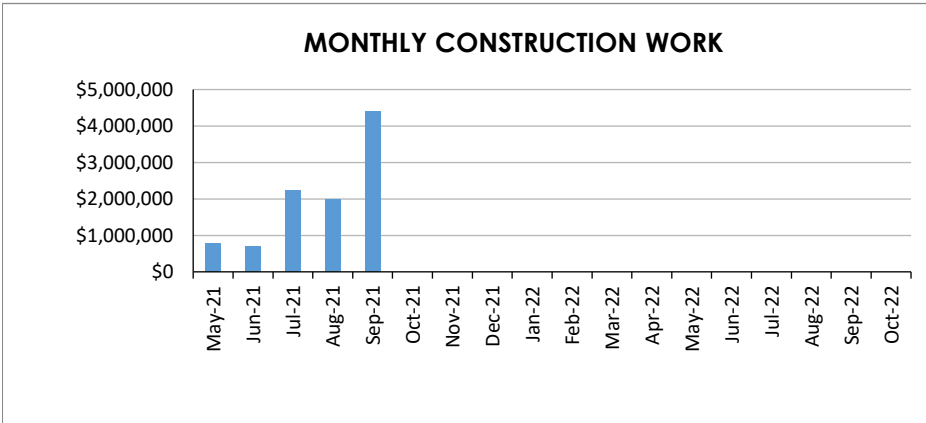

VALUE OF
WORK
COMPLETED
TO DATE:
\$10,087,162

PERCENT
OF
PROJECT
COMPLETE:
24%

