

DICK SCOBEE ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



April 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 1041 14th St. NE, Auburn.

Capacity: 38 classrooms and 650 student capacity.


Size & Capacity: 74,961 square feet.

Schedule: Open new school September 2020.

Construction Cost: \$39,143,452

CURRENT PROGRESS

- > Site grading, sidewalks and curbs.
- > Exterior siding and windows.
- > Sheetrock and interior finishes.
- > Mechanical equipment and ductwork.
- > Plumbing fixture and trim.
- > Electrical cabling, fixtures and trim.

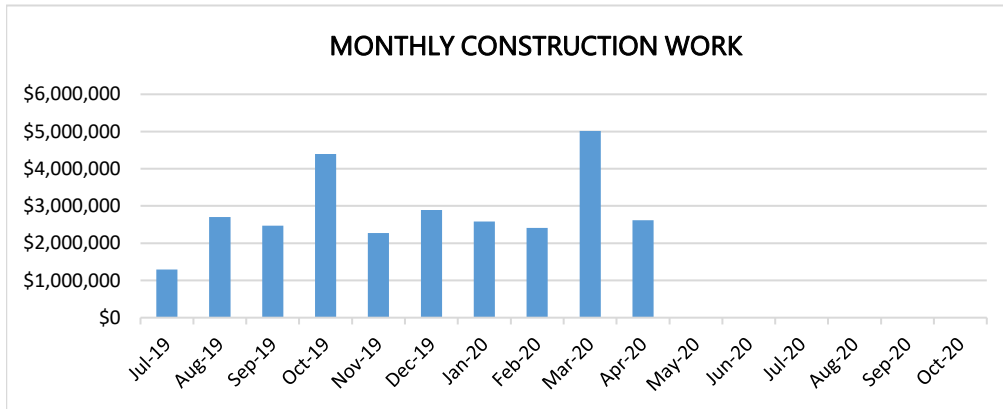

VALUE OF
WORK
COMPLETED
TO DATE:
\$28,655,059

PERCENT
OF
PROJECT
COMPLETE:
73%

