

DICK SCOBEE ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




SEPTEMBER 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 1041 14th St. NE, Auburn.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 74,961 square feet.
Schedule: Open new school September 2020.
Construction Cost: \$39,143,452

CURRENT PROGRESS

- > Punch list work.
- > Play equipment installation.
- > Mechanical & electrical systems adjustments.
- > Project close out document submittals.

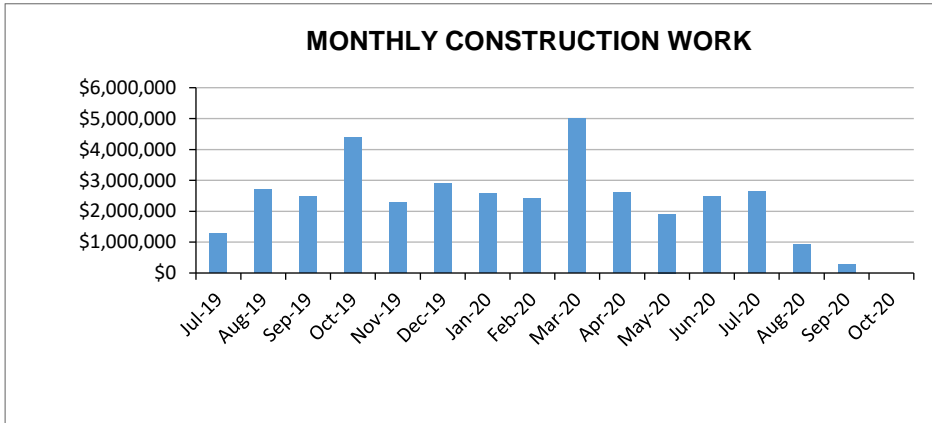

VALUE OF
WORK
COMPLETED
TO DATE:
\$36,867,087

PERCENT
OF
PROJECT
COMPLETE:
94%

