

DICK SCOBEE ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




FEBRUARY 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 1041 14th St. NE, Auburn.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 74,961 square feet
Schedule: Open new school September 2020.
Construction Cost: \$39,143,452

CURRENT PROGRESS

- > Permanent roof.
- > Exterior wall insulation and metal siding.
- > Exterior windows.
- > Interior wall framing and wallboard.
- > Mechanical and electrical rough-in.

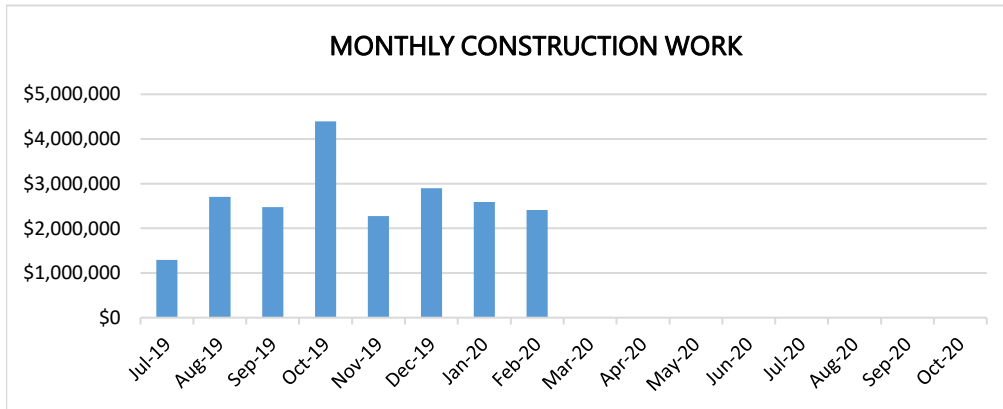

VALUE OF WORK COMPLETED TO DATE:
\$21,023,239

PERCENT OF PROJECT COMPLETE:
54%

