

DICK SCOBEE ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



June 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 1041 14th St. NE, Auburn.

Capacity: 38 classrooms and 650 student capacity.


Size & Capacity: 74,961 square feet.

Schedule: Open new school September 2020.

Construction Cost: \$39,143,452

CURRENT PROGRESS

- > Landscaping, sidewalks and asphalt paving.
- > Synthetic turf field preparation.
- > Interior finish work, cabinets and carpet.
- > Mech. and elec. equipment and finish work.
- > Kitchen equipment.
- > Mech. and elec. rough-in and finish work.

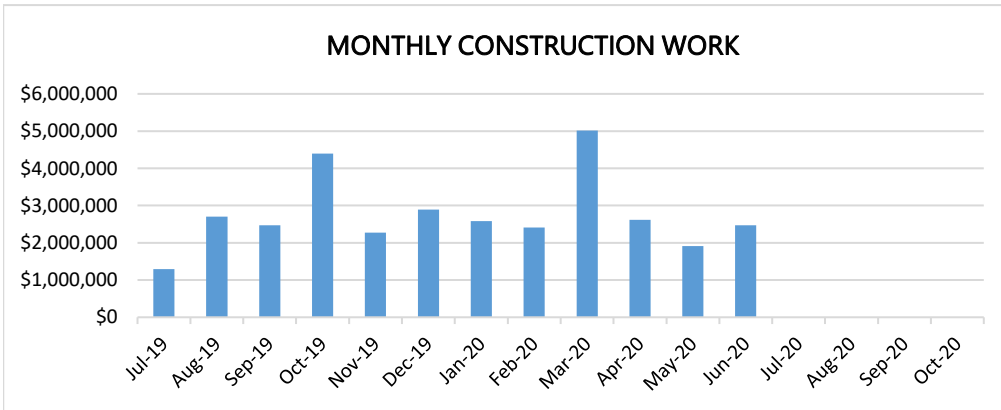

VALUE OF WORK COMPLETED TO DATE:
\$33,035,913

PERCENT OF PROJECT COMPLETE:
84%

