

# BOWMAN CREEK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington




## JUNE 2020 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on property located at 5701 Kersey Way SE, Auburn.  
Capacity: 38 classrooms and 650 student capacity.  
Size: 74,413 square feet.  
Schedule: Open new school September 2020.  
Construction Cost: \$46,707,697

### CURRENT PROGRESS

- > Irrigation, sidewalks and asphalt paving.
- > Kersey Way roadway and utilities.
- > Exterior siding.
- > Interior finish work.
- > Mech. and elec. rough-in and finish work.
- > Mechanical equipment start-up.

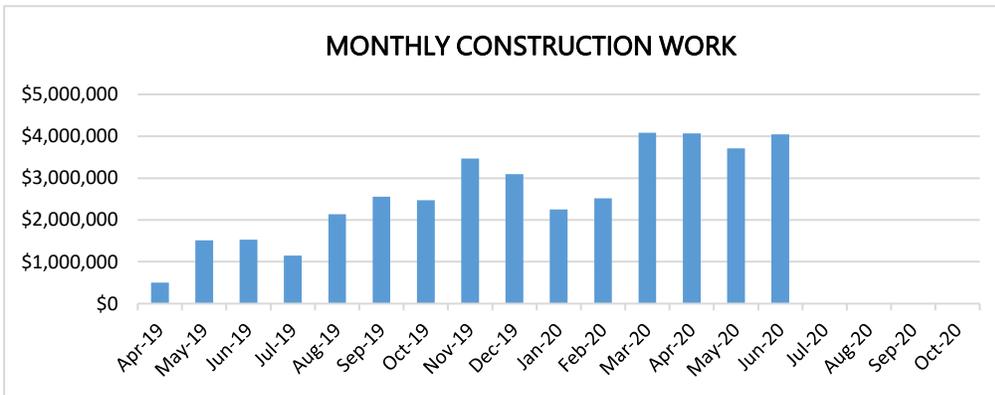

VALUE OF  
WORK  
COMPLETED  
TO DATE:  
**\$39,098,684**

PERCENT  
OF  
PROJECT  
COMPLETE:  
**84%**

