

# BOWMAN CREEK ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington



## APRIL 2020 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on property located at 5701 Kersey Way SE, Auburn.

Capacity: 38 classrooms and 650 student capacity.


Size: 74,413 square feet.

Schedule: Open new school September 2020.

Construction Cost: \$46,707,697

### CURRENT PROGRESS

- > Paving, curbs, sidewalks and fencing.
- > Turf playfield grading and drainage.
- > Exterior masonry.
- > Mechanical, electrical and plumbing work.
- > Interior framing, wallboard, painting & cabinets.
- > Metal roofing and exterior wall paneling.

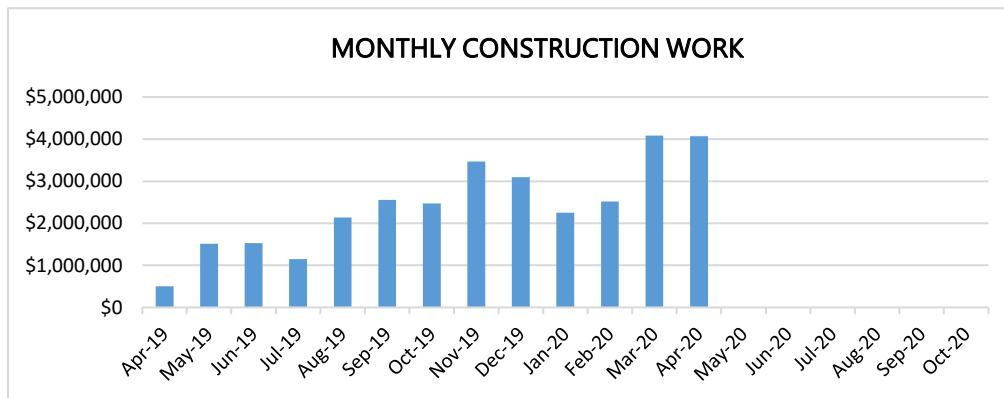

VALUE OF  
WORK  
COMPLETED  
TO DATE:  
**\$31,346,413**

PERCENT  
OF  
PROJECT  
COMPLETE:  
**67%**

