

BOWMAN CREEK ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



FEBRUARY 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on property located at 5701 Kersey Way SE, Auburn.

Capacity: 38 classrooms and 650 student capacity.


Size: 74,413 square feet.

Schedule: Open new school September 2020.

Construction Cost: \$46,707,697

CURRENT PROGRESS

- > Roadway electrical work.
- > Playshed concrete footings and slab.
- > Permanent roof.
- > Exterior insulation and windows.
- > Exterior brick.
- > Interior framing and wallboard.
- > Mechanical and electrical rough-in.

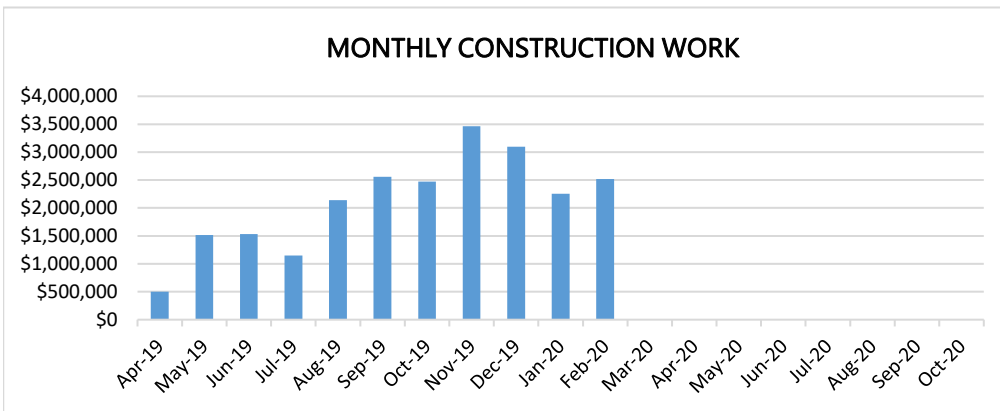

VALUE OF
WORK
COMPLETED
TO DATE:
\$23,194,524

PERCENT
OF
PROJECT
COMPLETE:
50%

