

LEA HILL ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




JULY 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 30908 124th Ave. SE, Auburn, WA
Capacity: 38 classrooms and 650 student capacity.
Size: 72,984 square feet.
Schedule: Open new school September 2022.
Construction Cost: \$42,300,090

CURRENT PROGRESS

- > Portable classroom removal.
- > Site clearing and excavation.
- > Hazardous materials abatement.
- > Building demolition.
- > Building footings and foundations.

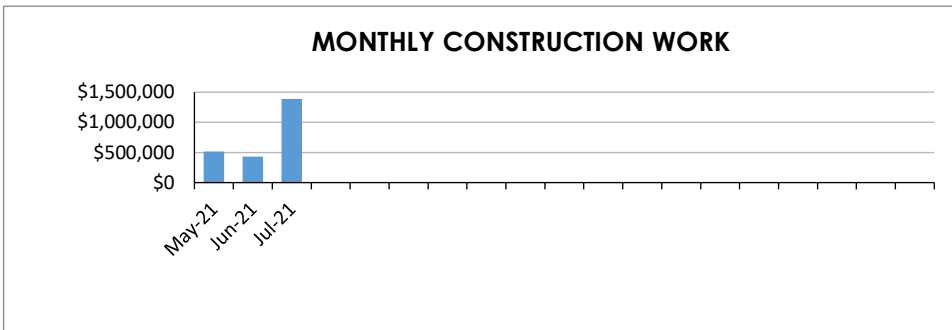

VALUE OF WORK
COMPLETED
TO DATE:

\$2,309,802

PERCENT OF
PROJECT COMPLETE:

5%

