

# OLYMPIC MIDDLE SCHOOL

Auburn School District No. 408  
Auburn, Washington



## FEBRUARY 2019 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

**Description:** Build new middle school at south end of school property and remodel existing building for use as an interim elementary school.


**Size & Capacity:** 106,000 square feet with 40 classrooms and 800 student capacity.

**Schedule:** Open new and remodeled school August 2019.

**Construction Cost:** \$53,580,000

### CURRENT PROGRESS

- > Interior & exterior wall framing.
- > Interior wall board and wall painting.
- > Exterior wall cover and insulation.
- > Mechanical and electrical rough-in.
- > Exterior brick veneer.
- > Roofing.

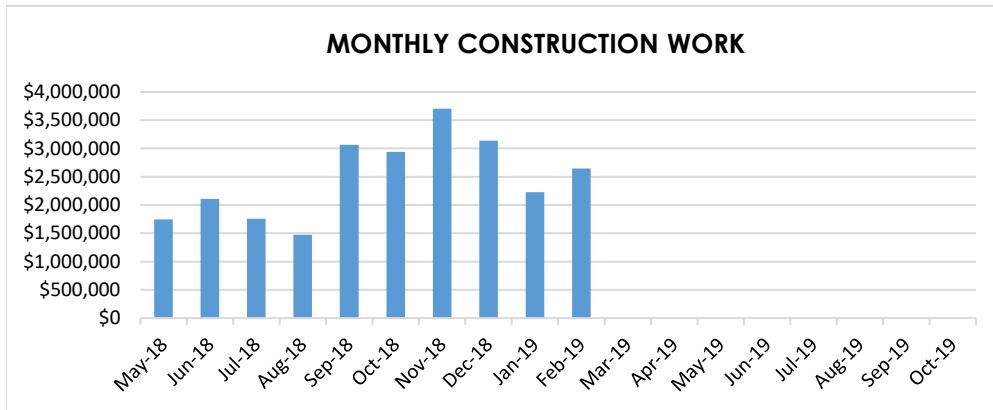

**VALUE OF WORK COMPLETED TO DATE:**  
**\$24,807,525**

**PERCENT OF PROJECT COMPLETE:**  
**46%**

