

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



SEPTEMBER 2020 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Underground utilities.
- > Parking lots.
- > Underground mechanical and electrical.
- > Concrete slabs.
- > Steel erection.

MONTHLY CONSTRUCTION WORK

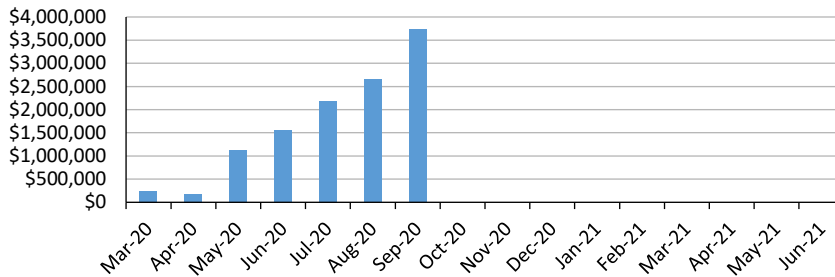

VALUE OF
WORK
COMPLETED
TO DATE:

\$11,677,564

PERCENT
OF
PROJECT
COMPLETE:

28%

