

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington



MAY 2021 CONSTRUCTION PROGRESS REPORT


PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Landscaping and sidewalks.
- > Synthetic turf curbs and drainage system.
- > Roof gutters and flashing.
- > Interior painting, flooring and ceilings.
- > Kitchen and mechanical equipment.
- > Mechanical & electrical connections and trim.

MONTHLY CONSTRUCTION WORK

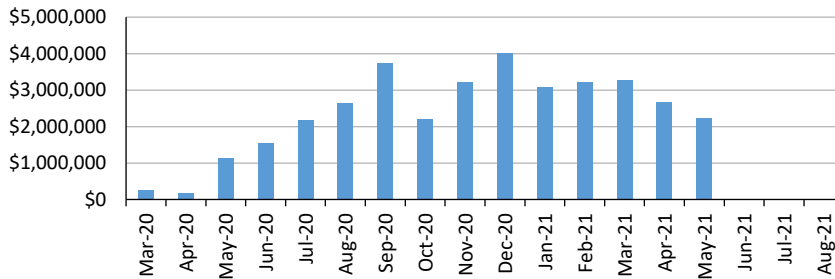

VALUE OF
WORK
COMPLETED
TO DATE:
\$35,576,565

PERCENT
OF
PROJECT
COMPLETE:
86%

