

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




NOVEMBER 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Curbs and sidewalks.
- > Steel erection and metal roof decking.
- > Exterior and interior wall framing.
- > Exterior sheathing.
- > Mechanical and electrical rough-in.
- > Gypsum wallboard.

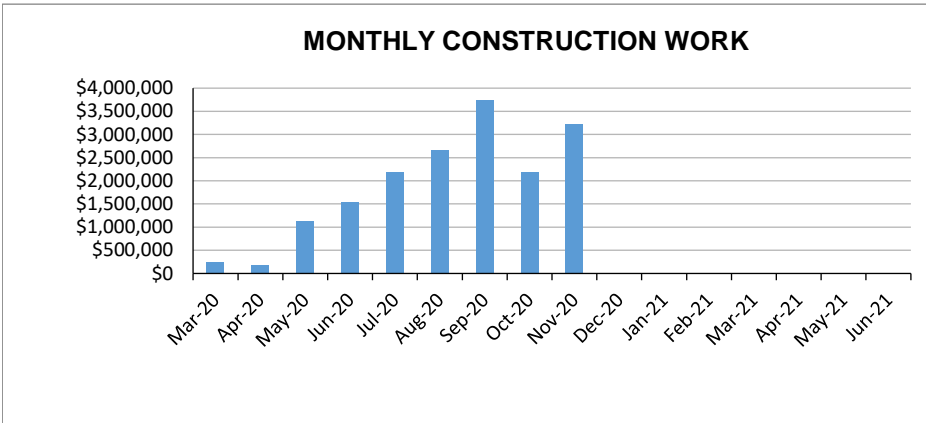

VALUE OF WORK COMPLETED TO DATE:
\$17,104,096

PERCENT OF PROJECT COMPLETE:
41%

