

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




JANUARY 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Metal roofing.
- > Exterior siding.
- > Interior insulation and drywall.
- > Painting.
- > Mechanical and electrical rough-in.
- > Fencing and landscape plantings.

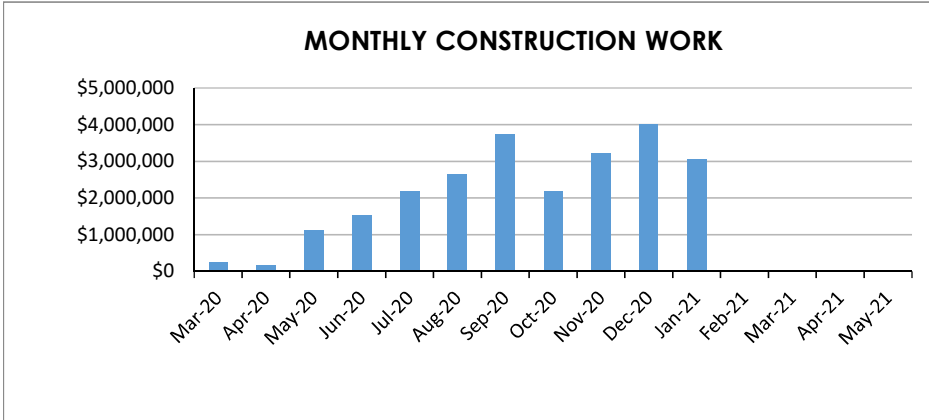

VALUE OF WORK COMPLETED TO DATE:
\$24,185,643

PERCENT OF PROJECT COMPLETE:
58%

