

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




FEBRUARY 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Landscaping.
- > Metal roofing.
- > Classroom cabinet delivery.
- > Gypsum board and painting.
- > Walk-in cooler and freezer.
- > Plumbing, HVAC and electrical rough-in.

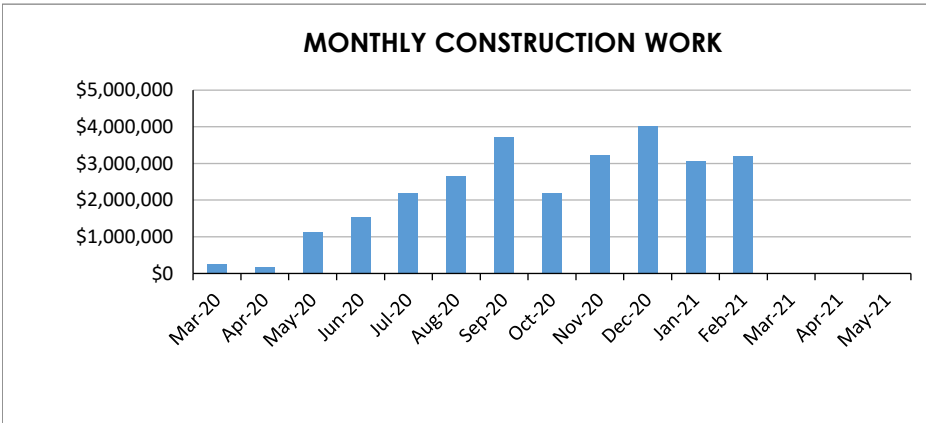

VALUE OF WORK COMPLETED TO DATE:
\$27,395,008

PERCENT OF PROJECT COMPLETE:
66%

