

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




MARCH 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Landscaping.
- > Metal roofing and exterior siding.
- > Interior insulation and sheet rock.
- > Ceiling grid and cabinets.
- > Painting.
- > Mechanical, electrical and plumbing.

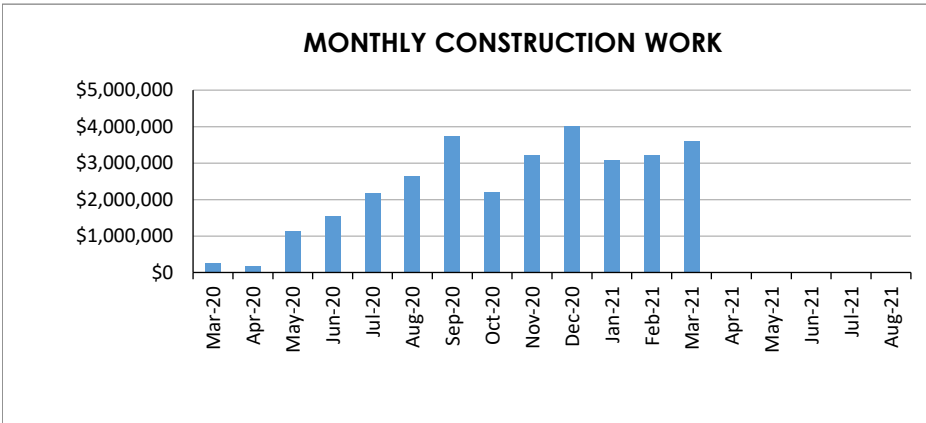

VALUE OF WORK COMPLETED TO DATE:
\$30,994,758

PERCENT OF PROJECT COMPLETE:
75%

