

# PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408  
Auburn, Washington




## JULY 2021 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.  
Capacity: 38 classrooms and 650 student capacity.  
Size & Capacity: 72,097 square feet.  
Schedule: Open new school September 2021.  
Construction Cost: \$41,390,816

### CURRENT PROGRESS

- > Lawn and irrigation system.
- > Stair treads and floor tile.
- > Elevator.
- > Mechanical equipment testing and balancing.
- > Access control, fire, and security systems.
- > Data, telephone, and intercom systems.

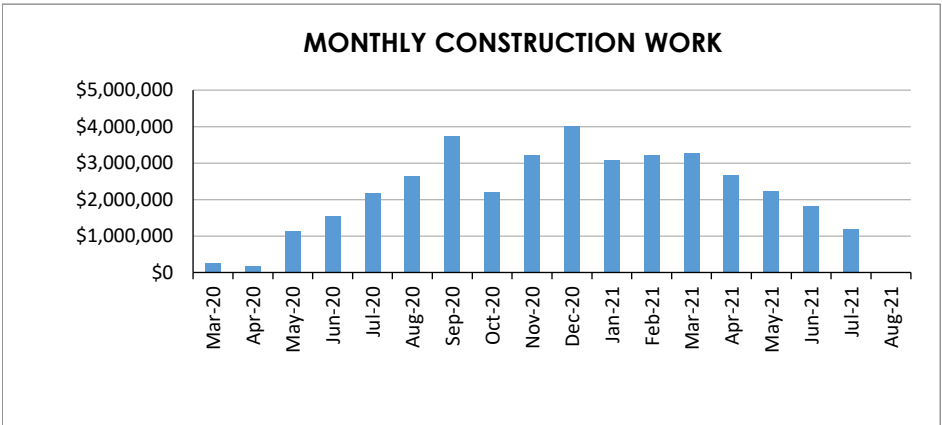

**VALUE OF WORK COMPLETED TO DATE:**  
**\$38,578,673**

**PERCENT OF PROJECT COMPLETE:**  
**93%**

