

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408

Auburn, Washington



AUGUST 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.

Capacity: 38 classrooms and 650 student capacity.

Size & Capacity: 72,097 square feet.


Schedule: Open new school September 2021.

Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Building technology systems and equipment.
- > Final keying.
- > Punch list and building commissioning.
- > Furniture and equipment move in.
- > Owner training.

MONTHLY CONSTRUCTION WORK

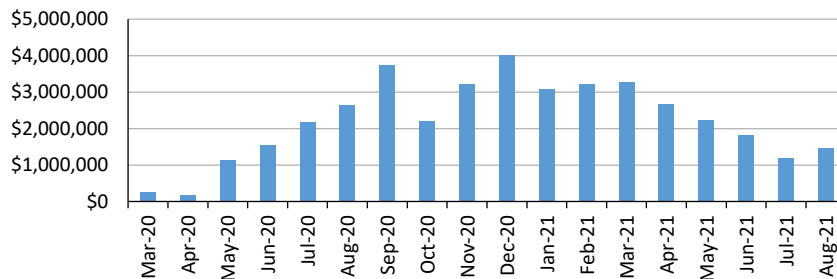

VALUE OF
WORK
COMPLETED
TO DATE:

\$40,034,650

PERCENT
OF
PROJECT
COMPLETE:

97%

