

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




SEPTEMBER 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,340,126

CURRENT PROGRESS

- > Punch list work.
- > Mechanical systems commissioning.
- > Electrical & irrigation systems commissioning.
- > Owner training.

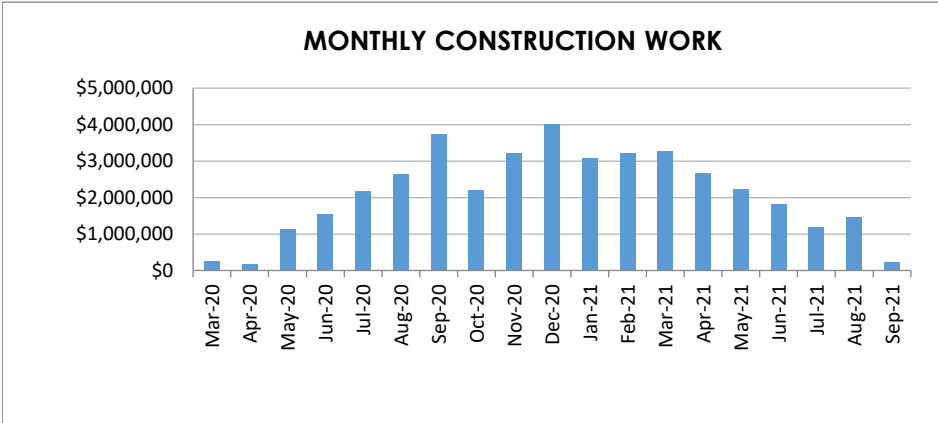

VALUE OF WORK COMPLETED TO DATE:
\$40,279,598

PERCENT OF PROJECT COMPLETE:
97%

