

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




DECEMBER 2020 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Metal roof decking.
- > Roof insulation and water-barrier.
- > Exterior wall insulation and windows.
- > Exterior masonry.
- > Interior wall framing.
- > Mechanical and electrical rough-in.

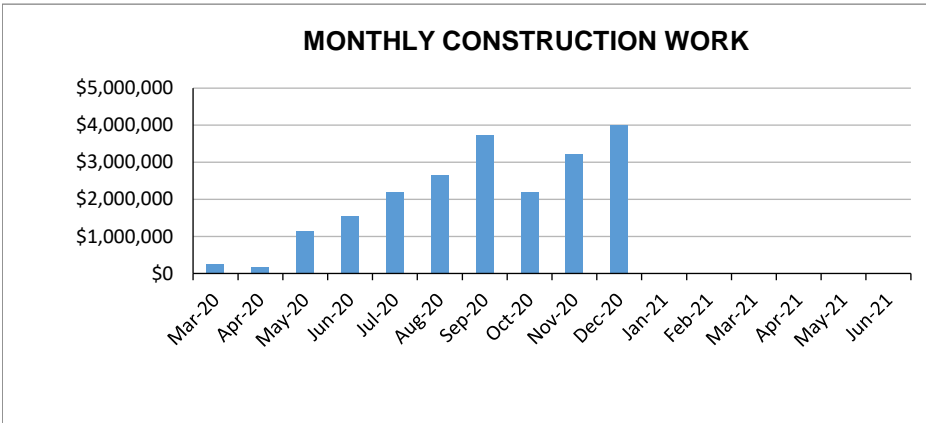

VALUE OF WORK COMPLETED TO DATE:
\$21,113,478

PERCENT OF PROJECT COMPLETE:
51%

