

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




JUNE 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Asphalt paving, landscaping and irrigation.
- > Turf playfield and playground equipment.
- > Interior painting, flooring, and ceilings.
- > Cabinets and markerboards.
- > Kitchen and mechanical equipment start-up.
- > Telecommunications & elec. systems start-up.

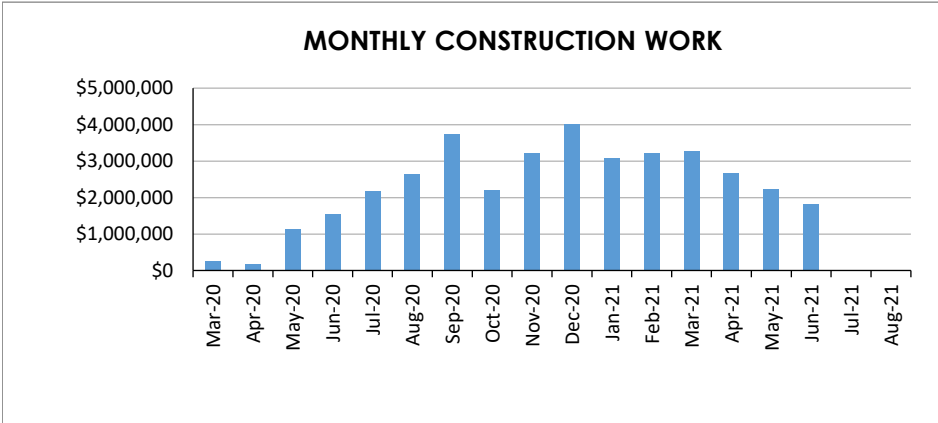

VALUE OF WORK COMPLETED TO DATE:
\$37,400,165

PERCENT OF PROJECT COMPLETE:
90%

