

PIONEER ELEMENTARY SCHOOL

Auburn School District No. 408
Auburn, Washington




APRIL 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on existing school property at 2301 M Street SE, Auburn, WA 98002.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 72,097 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$41,390,816

CURRENT PROGRESS

- > Curbs and sidewalks.
- > Playfield grading and perimeter drains.
- > Roof gutters and flashing.
- > Painting, ceilings, lockers and cabinets.
- > Monument sign and readerboard.
- > Mechanical and electrical.

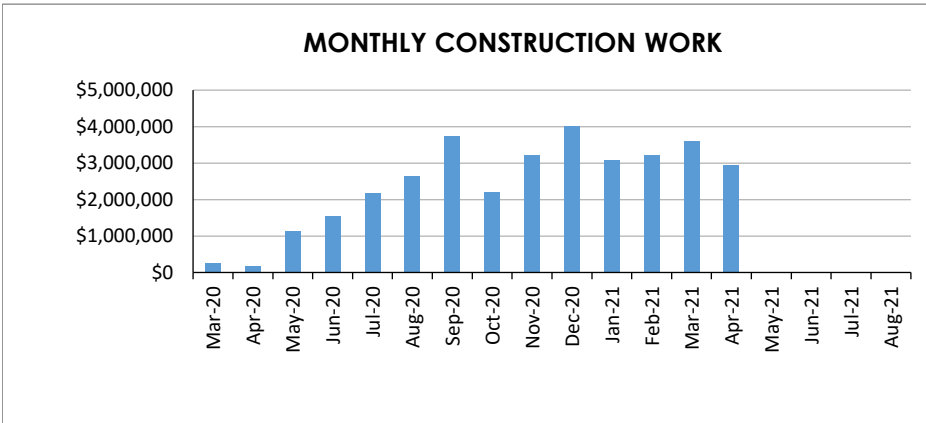

VALUE OF WORK COMPLETED TO DATE:
\$33,946,691

PERCENT OF PROJECT COMPLETE:
82%

