

ELEMENTARY SCHOOL NO. 16

Auburn School District No. 408 - Auburn, Washington
 Auburn, Washington




MAY 2021 CONSTRUCTION PROGRESS REPORT

PROJECT DATA

Description: Build new elementary school on property located at 13002 SE 304th ST, Auburn, WA 98092.
Capacity: 38 classrooms and 650 student capacity.
Size & Capacity: 73,052 square feet.
Schedule: Open new school September 2021.
Construction Cost: \$44,226,245

CURRENT PROGRESS

- > Site landscaping, sidewalks and roadway.
- > Precast concrete and masonry.
- > Metal roofing and cabinets.
- > Interior painting, flooring and ceilings.
- > Food service and mechanical equipment.
- > Mechanical & electrical connections and trim.

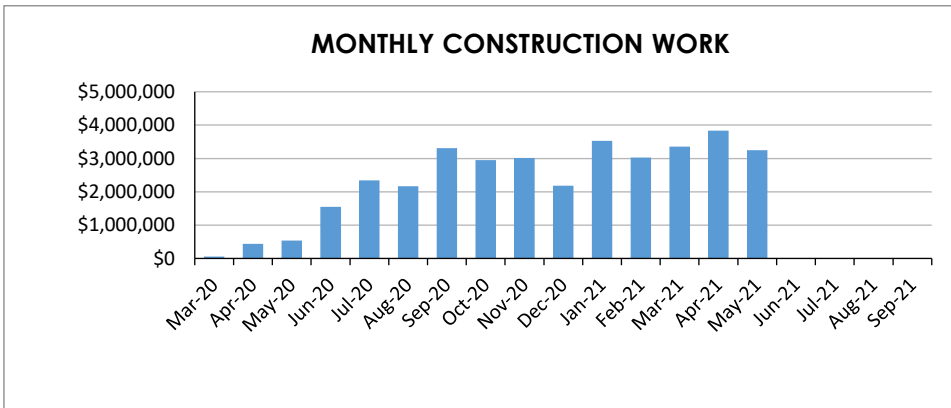

VALUE OF WORK COMPLETED TO DATE:
\$35,306,880

PERCENT OF PROJECT COMPLETE:
80%

