

# ELEMENTARY SCHOOL NO. 16

Auburn School District No. 408 - Auburn, Washington  
 Auburn, Washington




## AUGUST 2021 CONSTRUCTION PROGRESS REPORT

### PROJECT DATA

Description: Build new elementary school on property located at 13002 SE 304th ST, Auburn, WA 98092.  
 Capacity: 38 classrooms and 650 student capacity.  
 Size & Capacity: 73,052 square feet.  
 Schedule: Open new school September 2021.  
 Construction Cost: \$44,226,245

### CURRENT PROGRESS

- > Asphalt paving.
- > Building technology systems and equipment.
- > Final keying.
- > Punch list and building commissioning.
- > Furniture and equipment move in.
- > Owner training.

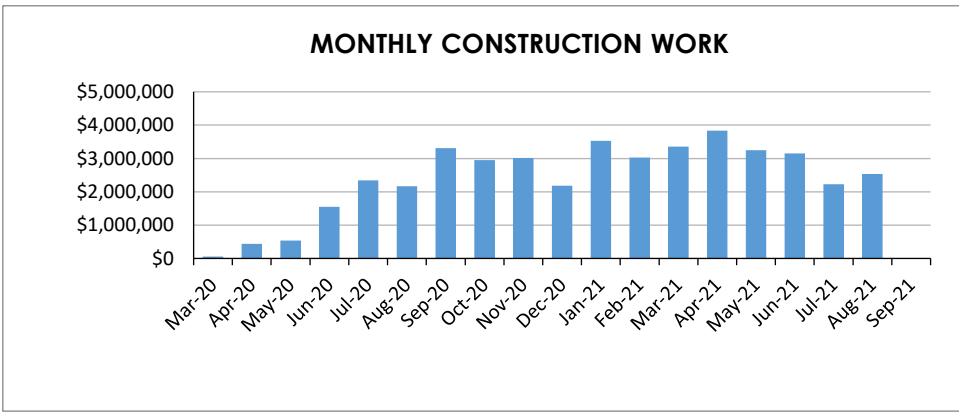

**VALUE OF WORK COMPLETED TO DATE:**  
**\$43,173,864**

**PERCENT OF PROJECT COMPLETE:**  
**98%**

